


#	Name	%	Start Date	Completion Date	2009	2010
1	Project 2006-08 Transmission Loading Relief	80.8%	7/8/09 8:00 AM	9/17/10 5:00 PM		81
2	TODAY	100.0%	7/8/09 8:00 AM	7/8/09 8:00 AM	100%, 7/8/09	
3	Standard Development - PHASE 2	100.0%	7/8/09 9:00 AM	10/31/09 9:00 AM	100%, 10/31/09	
4	Conduct Field Test	100.0%	7/8/09 9:00 AM	10/31/09 9:00 AM	100%, 10/31/09	
5	Standard Development - PHASE 3	100.0%	7/8/09 9:00 AM	6/24/10 9:00 AM		100%, 6/24/10
6	Develop Third Draft of Standard(s)	100.0%	7/8/09 9:00 AM	8/14/09 9:00 AM	100%, 8/14/09	
7	Re-submit Draft Documents for NERC Staff Review	100.0%	7/8/09 9:00 AM	7/14/09 5:00 PM	100%, 7/14/09	
8	Third Posting of Documents for Industry Comment	100.0%	7/15/09 9:00 AM	8/14/09 9:00 AM	100%, 8/14/09	
9	Develop Fourth Draft of stadnards(s)	100.0%	8/14/09 9:00 AM	11/25/09 9:00 AM	100%, 11/25/09	
10	Develop Reply Comments and Fourth Draft of Standard	100.0%	8/14/09 9:00 AM	9/24/09 5:00 PM	100%, 9/24/09	
11	Submit Draft Documents for NERC Staff Review	100.0%	9/25/09 9:00 AM	10/21/09 5:00 PM	100%, 10/21/09	
12	Fourth Posting of Documents for Industry Comment	100.0%	10/22/09 9:00 AM	11/25/09 9:00 AM	100%, 11/25/09	
13	Balloting	100.0%	11/25/09 9:00 AM	6/24/10 9:00 AM		100%, 6/24/10
14	Prepare Documents for Balloting	100.0%	11/25/09 9:00 AM	2/16/10 5:00 PM		100%, 2/16/10
15	Submit Draft Documents for NERC Staff Review	100.0%	2/17/10 9:00 AM	2/23/10 5:00 PM		100%, 2/23/10
16	Revise Documents Based on NERC Staff Review	100.0%	2/24/10 9:00 AM	3/2/10 5:00 PM		100%, 3/2/10
17	Re-submit Draft Documents for NERC Staff Review	100.0%	3/3/10 9:00 AM	3/9/10 5:00 PM		100%, 3/9/10
18	Seek SC Approval to move to Ballot	100.0%	3/10/10 9:00 AM	3/16/10 5:00 PM		100%, 3/16/10
19	Receive SC Approval to Move to Ballot	100.0%	3/17/10 9:00 AM	3/23/10 5:00 PM		100%, 3/23/10
20	Project Moved to Balloting Phase	100.0%	3/23/10 5:00 PM	3/23/10 5:00 PM		100%, 3/23/10
21	30-Day Pre-ballot Review	100.0%	3/24/10 9:00 AM	4/23/10 9:00 AM		100%, 4/23/10
22	Initial Ballot	100.0%	4/23/10 9:00 AM	5/3/10 9:00 AM		100%, 5/3/10
23	Develop Reply Comments for Negatives Ballots	100.0%	5/3/10 9:00 AM	5/21/10 5:00 PM		100%, 5/21/10
24	Submit Draft Documents for Quality Review	100.0%	5/24/10 9:00 AM	5/28/10 5:00 PM		100%, 5/28/10
25	Revise Documents Based on Quality Review	100.0%	5/31/10 9:00 AM	6/4/10 5:00 PM		100%, 6/4/10
26	Re-submit Draft Documents for Quality Review	100.0%	6/7/10 9:00 AM	6/11/10 5:00 PM		100%, 6/11/10
27	Recirculation Ballot	100.0%	6/14/10 9:00 AM	6/24/10 9:00 AM		100%, 6/24/10
28	Standard Development Phase Complete	100.0%	6/24/10 9:00 AM	6/24/10 9:00 AM		100%, 6/24/10
29	NERC BOT Approval	100.0%	4/23/10 9:00 AM	9/3/10 5:00 PM		100%

Project: Project 2006-08 Transmission Loading Relief
Planned Start: 6/19/09 Projected Start: 7/8/09
Planned Completion: 9/17/10 Projected Completion: 2/23/11
Printed On: 11/19/10


Page 1

Ensures that critical transmission system limits are relieved within 30 minutes. The TLR project has been divided into three phases:

Phase 1 — A coordinated effort with NAESB to clarify and refine the steps in the



#	Name	%	Start Date	Completion Date	2009	2010
30	Meet to Discuss Document Preparation	100.0%	4/23/10 9:00 AM	5/20/10 5:00 PM		100%, 5/20/10
31	Prepare BOT Material (Coordinator)	100.0%	5/21/10 9:00 AM	6/24/10 5:00 PM		100%, 6/24/10
32	Finalize BOT Material (VP)	100.0%	6/25/10 9:00 AM	7/8/10 5:00 PM		100%, 7/8/10
33	Post for 30 Days Prior to BOT Meeting	100.0%	7/9/10 9:00 AM	8/8/10 9:00 AM		100%, 8/8/10
34	Receive BOT Approval	100.0%	8/9/10 9:00 AM	9/3/10 5:00 PM		100%, 9/3/10
35	Regulatory Filings	2.9%	4/23/10 9:00 AM	9/17/10 5:00 PM		3%
36	Develop Initial Draft of Regulatory Filings (Coordinator)	10.0%	4/23/10 9:00 AM	5/20/10 5:00 PM		10%, 5/20/10
37	Finalize Standards' Version of the Draft Regulatory Filings	0.0%	5/21/10 9:00 AM	6/17/10 5:00 PM		0%, 6/17/10
38	Legal and Management Review of Regulatory Filings	0.0%	6/18/10 9:00 AM	7/15/10 5:00 PM		0%, 7/15/10
39	File Documents with Appropriate Regulatory Authorities	0.0%	9/6/10 9:00 AM	9/17/10 5:00 PM		0%
40	Project and Filing Complete	0.0%	9/17/10 5:00 PM	9/17/10 5:00 PM		0%

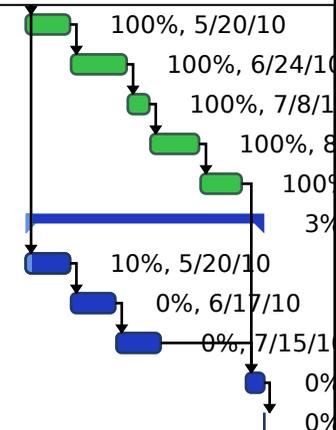

Project: Project 2006-08 Transmission Loading Relief
Planned Start: 6/19/09 Projected Start: 7/8/09
Planned Completion: 9/17/10 Projected Completion: 2/23/11
Printed On: 11/19/10

Ensures that critical transmission system limits are relieved within 30 minutes. The TLR project has been divided into three phases:
Phase 1 — A coordinated effort with NAESB to clarify and refine the steps in the

Planned		Overdue	
Critical Path		In Progress	
Summary		Complete	
Milestone		Predecessor	


	2011	2012	2013	2014
% 9/17/10				
% 9/3/10				

Project: Project 2006-08 Transmission Loading Relief
 Planned Start: 6/19/09 Projected Start: 7/8/09
 Planned Completion: 9/17/10 Projected Completion: 2/23/11
 Printed On: 11/19/10

Ensures that critical transmission system limits are relieved within 30 minutes. The TLR project has been divided into three phases:
 Phase 1 — A coordinated effort with NAESB to clarify and refine the steps in the

Planned		Overdue	
Critical Path		In Progress	
Summary		Complete	
Milestone		Predecessor	

	2011	2012	2013	2014
0 0 /8/10 %, 9/3/10 , 9/17/10 0 , 9/17/10 , 9/17/10				



Project: Project 2006-08 Transmission Loading Relief
 Planned Start: 6/19/09 Projected Start: 7/8/09
 Planned Completion: 9/17/10 Projected Completion: 2/23/11
 Printed On: 11/19/10

Page 4

Ensures that critical transmission system limits are relieved within 30 minutes. The TLR project has been divided into three phases:

Phase 1 — A coordinated effort with NAESB to clarify and refine the steps in the

Planned		Overdue	
Critical Path		In Progress	
Summary		Complete	
Milestone		Predecessor	
