


ID	Task Name	Duration	Start	Finish	Predecessors	4th Quarter			1st Quarter					
						Sep	Oct	Nov	Dec	Jan	Feb	Mar		
1	SRBSDT: Project 2006-03	690 days?	Thu 10/26/06	Wed 6/17/09										
2	SAR Development	119 days	Thu 10/26/06	Tue 4/10/07										
3	Step 1a - draft SAR	1 day	Thu 10/26/06	Thu 10/26/06										
4	Step 1b - appoint SAR DT	12 days	Mon 11/6/06	Tue 11/21/06										
5	Step 2a - post for comment	22 days	Mon 11/6/06	Tue 12/5/06										
6	Step 2b - address comments	46 days	Wed 12/6/06	Wed 2/7/07	5									
7	Step 3a - post for comment	22 days	Thu 2/8/07	Fri 3/9/07										
8	Step 3b - address comments	10 days	Mon 3/12/07	Fri 3/23/07										
9	Step 4 - SC approval	1 day	Tue 4/10/07	Tue 4/10/07										
10	Standard Development	566 days?	Wed 4/18/07	Wed 6/17/09										
11	Step 1 - appoint SDT	35 days	Wed 4/18/07	Tue 6/5/07										
12	Step 2 - draft standard	50 days	Wed 6/6/07	Tue 8/14/07	11									
13	Step 2a - post #1 for comment	33 days	Wed 8/15/07	Fri 9/28/07	12									
14	Step 3 - address comments	70 days	Mon 10/1/07	Fri 1/4/08	13									
15	Step 3a -post #2 for comments	22 days	Mon 1/7/08	Tue 2/5/08	14									
16	Step 3b - address comments	38 days?	Wed 2/6/08	Fri 3/28/08	15									
17	Step 3c -submit to staff	8 days?	Mon 3/31/08	Wed 4/9/08	16									
18	Step 3d -address comments	3 days?	Thu 4/10/08	Mon 4/14/08	17									
19	Step 3e - post #3 for comments	33 days?	Tue 4/15/08	Thu 5/29/08	18									
20	Step 4 - address comments	66 days?	Fri 5/30/08	Fri 8/29/08	19									
21	Step 4a - submit to staff	10 days?	Wed 9/3/08	Tue 9/16/08	20									
22	Step 4b - address comments	10 days?	Tue 10/7/08	Mon 10/20/08	21									
23	Step 4c - post #4 for comments	21 days	Tue 10/21/08	Tue 11/18/08	22									
24	Step 5 - address comments	30 days?	Thu 1/8/09	Wed 2/18/09	23									
25	Step 6 - pre-ballot period	22 days	Mon 3/16/09	Tue 4/14/09										
26	Step 6 - ballot	30 days?	Wed 4/15/09	Tue 5/26/09	25									
27	Step 6a - address comments	5 days?	Wed 5/27/09	Tue 6/2/09	26									
28	Step 7 - reballot	10 days?	Wed 6/3/09	Tue 6/16/09	27									
29	Step 7 - submit to BOT	1 day?	Wed 6/17/09	Wed 6/17/09	28									

Project: srbsdt_project_schedule_200! Date: Fri 3/20/09	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

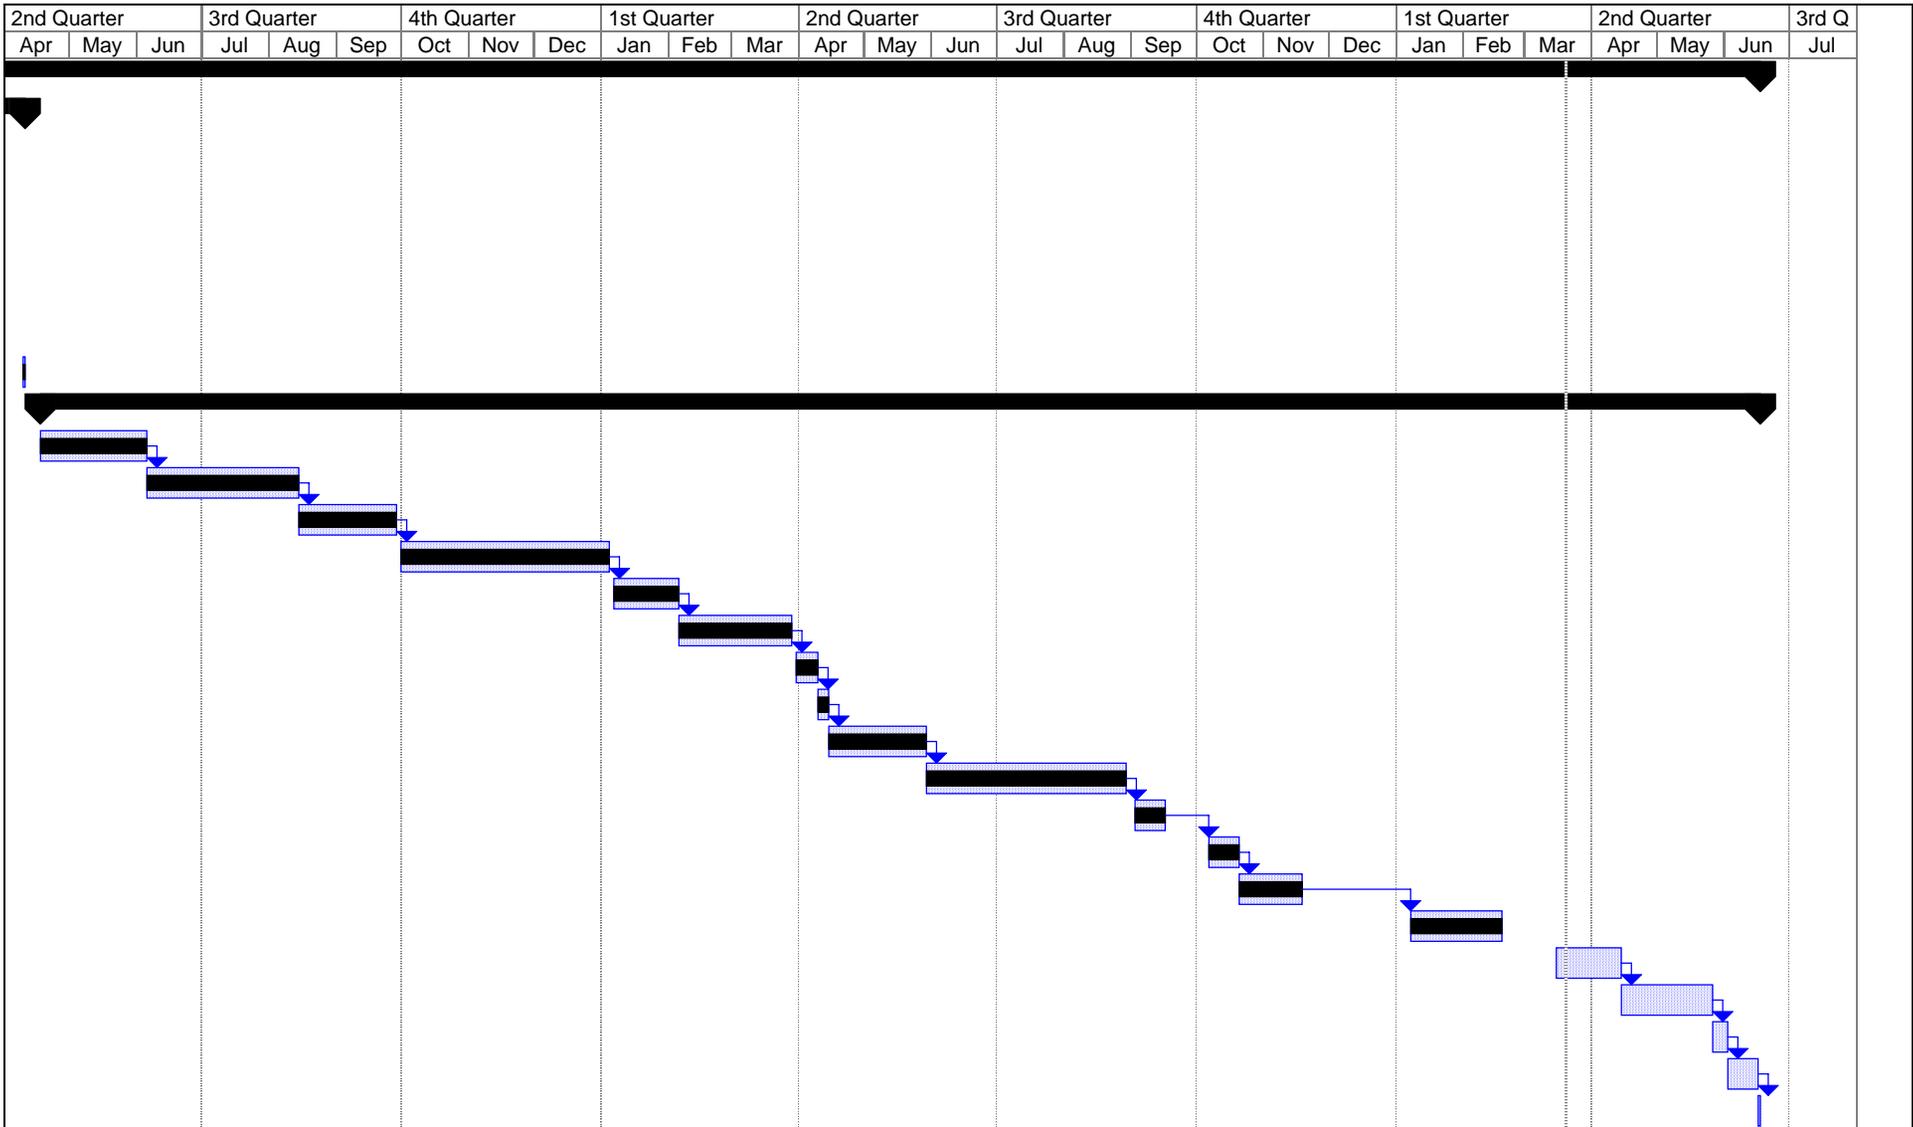

Project: srbsdt_project_schedule_200!
 Date: Fri 3/20/09

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
