Project 2010-13.3 – Relay Loadability: Power Swings (PRC-026-1)

	Task Name	Start	Finish
1	**Project 2010-13.3 Phase III - Relay Loadabi**	**Thu 2/21/13**	**Fri 12/12/14**
2	**Techincal Development**	**Thu 2/21/13**	**Fri 9/27/13**
9	**A - ASSEMBLE SDT**	**Wed 6/12/13**	**Wed 2/19/14**
15	**B - DRAFT STANDARD**	**Wed 2/19/14**	**Fri 4/18/14**
16	Kickoff and Write Draft Standard	Wed 2/19/14	Sat 4/5/14
17	Director Level Review	Mon 4/7/14	Fri 4/11/14
18	Finalize Documents	Mon 4/14/14	Fri 4/18/14
19	**E - COMMENT and BALLOT**	**Mon 4/21/14**	**Mon 6/9/14**
20	Posting Review	Mon 4/21/14	Mon 4/21/14
21	SC Approval to post	Tue 4/22/14	Tue 4/22/14
22	PRC-026-1 45-Day Comment Period Rl	Tue 4/22/14	Fri 6/6/14
23	Prepare Comment Report	Mon 6/9/14	Mon 6/9/14
24	**D - RESPOND TO COMMENTS**	**Tue 6/10/14**	**Tue 7/15/14**
25	Summary Responses	Tue 6/10/14	Mon 6/30/14
26	Director Level Review	Tue 7/1/14	Tue 7/8/14
27	Finalize Documents	Wed 7/9/14	Tue 7/15/14
28	**E - COMMENT and BALLOT**	**Wed 7/16/14**	**Tue 9/2/14**
29	Posting Review	Wed 7/16/14	Wed 7/16/14
30	PRC-026-1 Comment Period REF_BAL	Wed 7/16/14	Sat 8/30/14
31	Prepare Comment Report	Mon 9/1/14	Tue 9/2/14
32	**G - FINAL BALLOT**	**Wed 9/3/14**	**Sun 10/26/14**
33	Respond to Each Comment	Wed 9/3/14	Tue 9/30/14
34	Director Level Review	Wed 10/1/14	Tue 10/7/14
35	Finalize Documents	Wed 10/8/14	Wed 10/15/14
36	Posting Review	Thu 10/16/14	Thu 10/16/14
37	PRC-026-1 Final Ballot REF_BALLOT_	Thu 10/16/14	Sun 10/26/14
38	**H - BOT APPROVAL**	**Wed 9/3/14**	**Mon 11/17/14**
39	Develop Board Materials	Wed 9/3/14	Tue 9/9/14
40	Perform Standards Leadership Revie\	Wed 9/10/14	Wed 9/17/14
41	Perform Legal Review	Thu 9/18/14	Wed 9/24/14
42	Perform Exec Mgmt Review	Thu 9/25/14	Wed 10/1/14
43	Board Member Review	Wed 10/1/14	Sat 11/15/14
44	Board Vote on Materials	Mon 11/17/14	Mon 11/17/14
45	**I - FILING**	**Wed 9/3/14**	**Fri 12/12/14**
46	Draft Filing	Wed 9/3/14	Wed 9/17/14
47	Perform Regulatory Review	Thu 9/18/14	Mon 10/6/14
48	Perform Legal Review	Tue 10/7/14	Wed 10/22/14
49	Perform Exec Mgmt Review	Thu 10/23/14	Wed 11/5/14
50	Assemble Development Record	Thu 11/6/14	Wed 11/26/14
51	Assemble Filing Package	Thu 11/27/14	Fri 12/12/14
52	Submit Filing	Fri 12/12/14	Fri 12/12/14

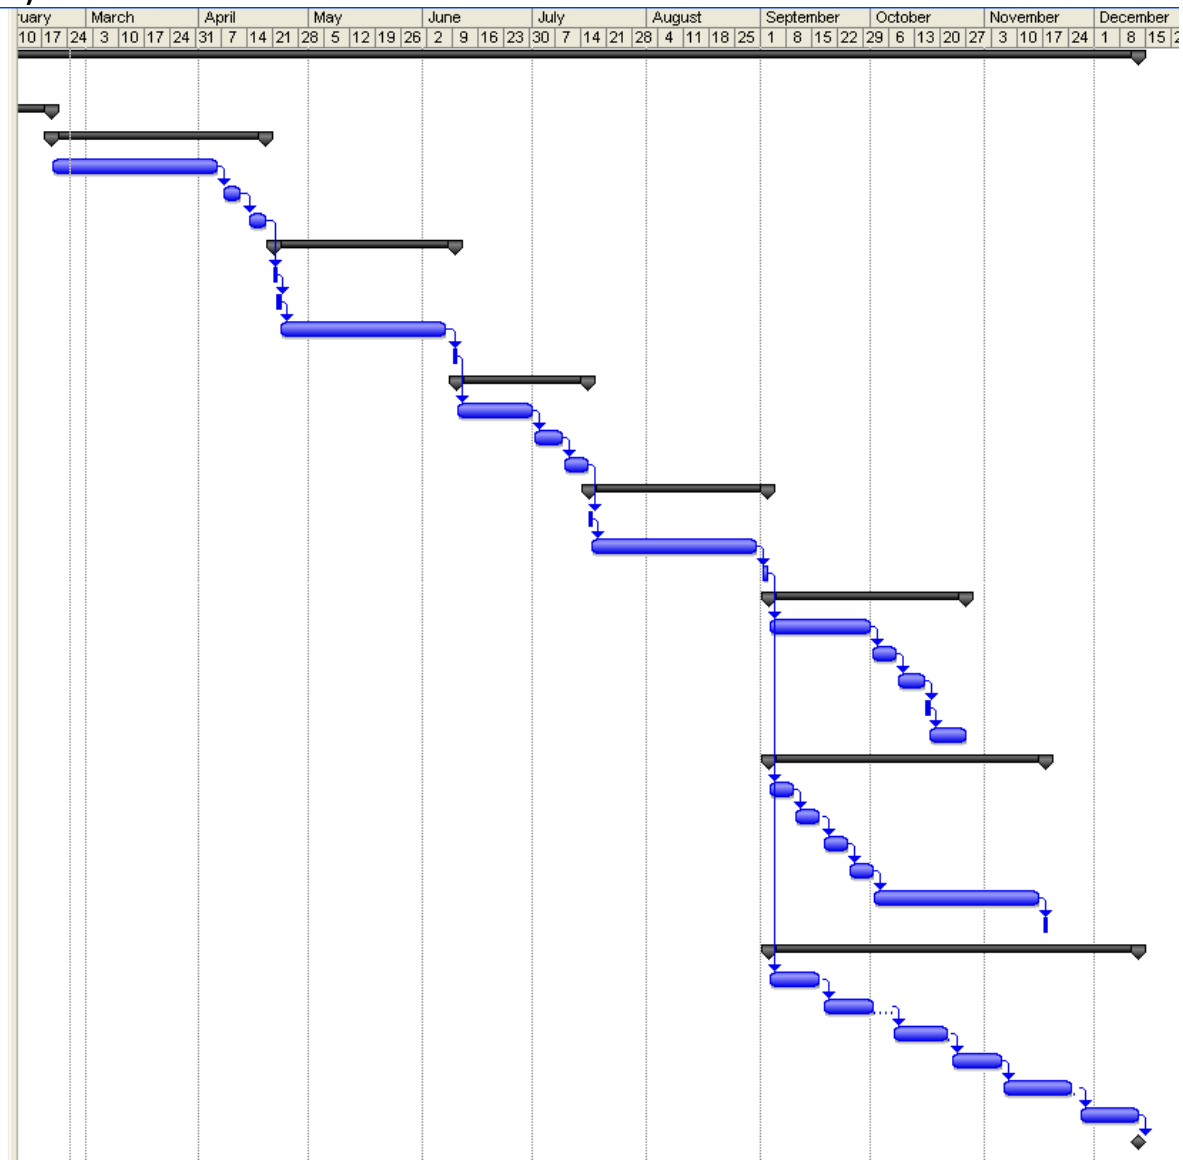

Schedule as of February 25, 2014
